




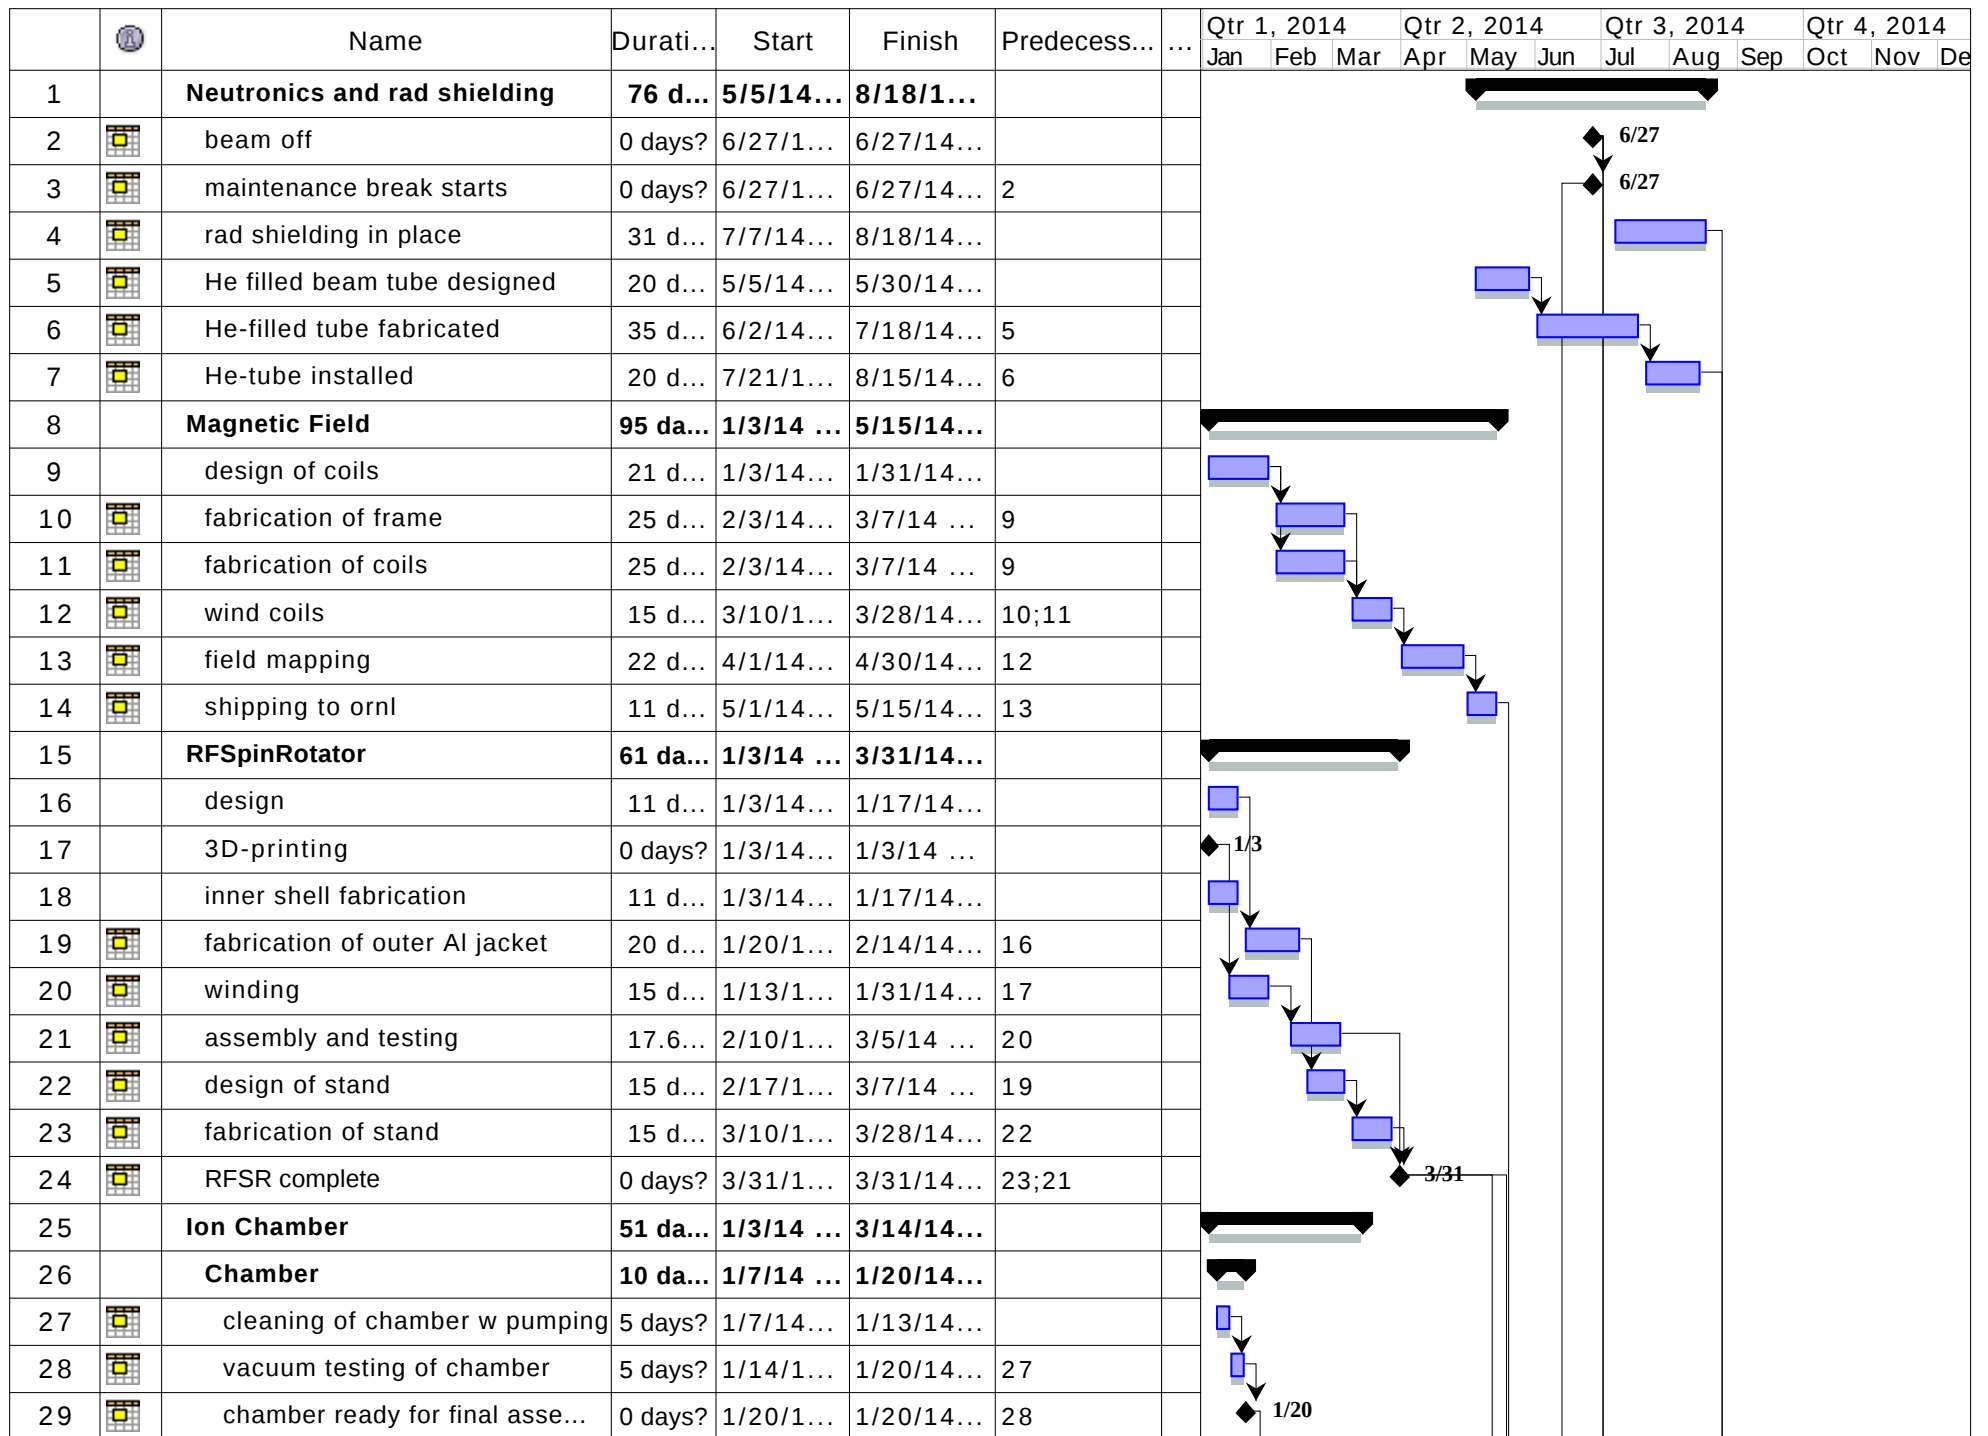

		Name	Durati...	Start	Finish	Predecess...	...	Qtr 1, 2014			Qtr 2, 2014			Qtr 3, 2014			Qtr 4, 2014		
								Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	De
30		Signal and HV frames	51 da...	1/3/14 ...	3/14/14...														
31		wiring frames	0 days?	1/3/14...	1/3/14 ...														
32		cleaning wired frames	0 days?	1/4/14...	1/6/14 ...	31													
33		PCB arrives	0 days?	1/24/1...	1/24/14...														
34		stacking and assembly	20 d...	1/27/1...	2/21/14...	33;32;29													
35		testing	15 d...	2/24/1...	3/14/14...	34													
36		chamber ready for electronic t...	0 days?	3/14/1...	3/14/14...	35;46													
37		Gas Handling system	43.5 ...	1/13/1...	3/13/14...														
38		design and test of concept	20 d...	1/13/1...	2/7/14 ...														
39		procurement	10 d...	2/10/1...	2/21/14...	38													
40		fabrication	10 d...	2/10/1...	2/21/14...	38													
41		assembly and testing	13.5 ...	2/24/1...	3/13/14...	39;40													
42		HV source	38.5 ...	1/20/1...	3/13/14...														
43		test concept	15 d...	1/20/1...	2/7/14 ...														
44		procurement and fab	13 d...	2/10/1...	2/26/14...	43													
45		testing with 4He	8.5 d...	3/3/14...	3/13/14...	44													
46		chamber ready electronic testi...	0 days?	3/13/1...	3/13/14...	45;41													
47		Preamplifiers	66 da...	1/3/14 ...	4/4/14 ...														
48		testing	21 d...	1/3/14...	1/31/14...														
49		proc power supply	15 d...	1/15/1...	2/5/14 ...														
50		complete preamp boards	15 d...	2/3/14...	2/21/14...	48													
51		procure cables for ADCs	30 d...	1/13/1...	2/21/14...														
52		Cooling	45 da...	1/13/1...	3/14/14...														
53		test cooling concept	15 d...	1/13/1...	1/31/14...														
54		design cooling	10 d...	2/3/14...	2/14/14...	53													
55		procure/fab cooling	10 d...	2/17/1...	2/28/14...	54													
56		test with slow controls	10 d...	3/3/14...	3/14/14...	55													
57		Enclosure	59 da...	1/14/1...	4/4/14 ...														
58		design of enclosure	24 d...	1/14/1...	2/14/14...														

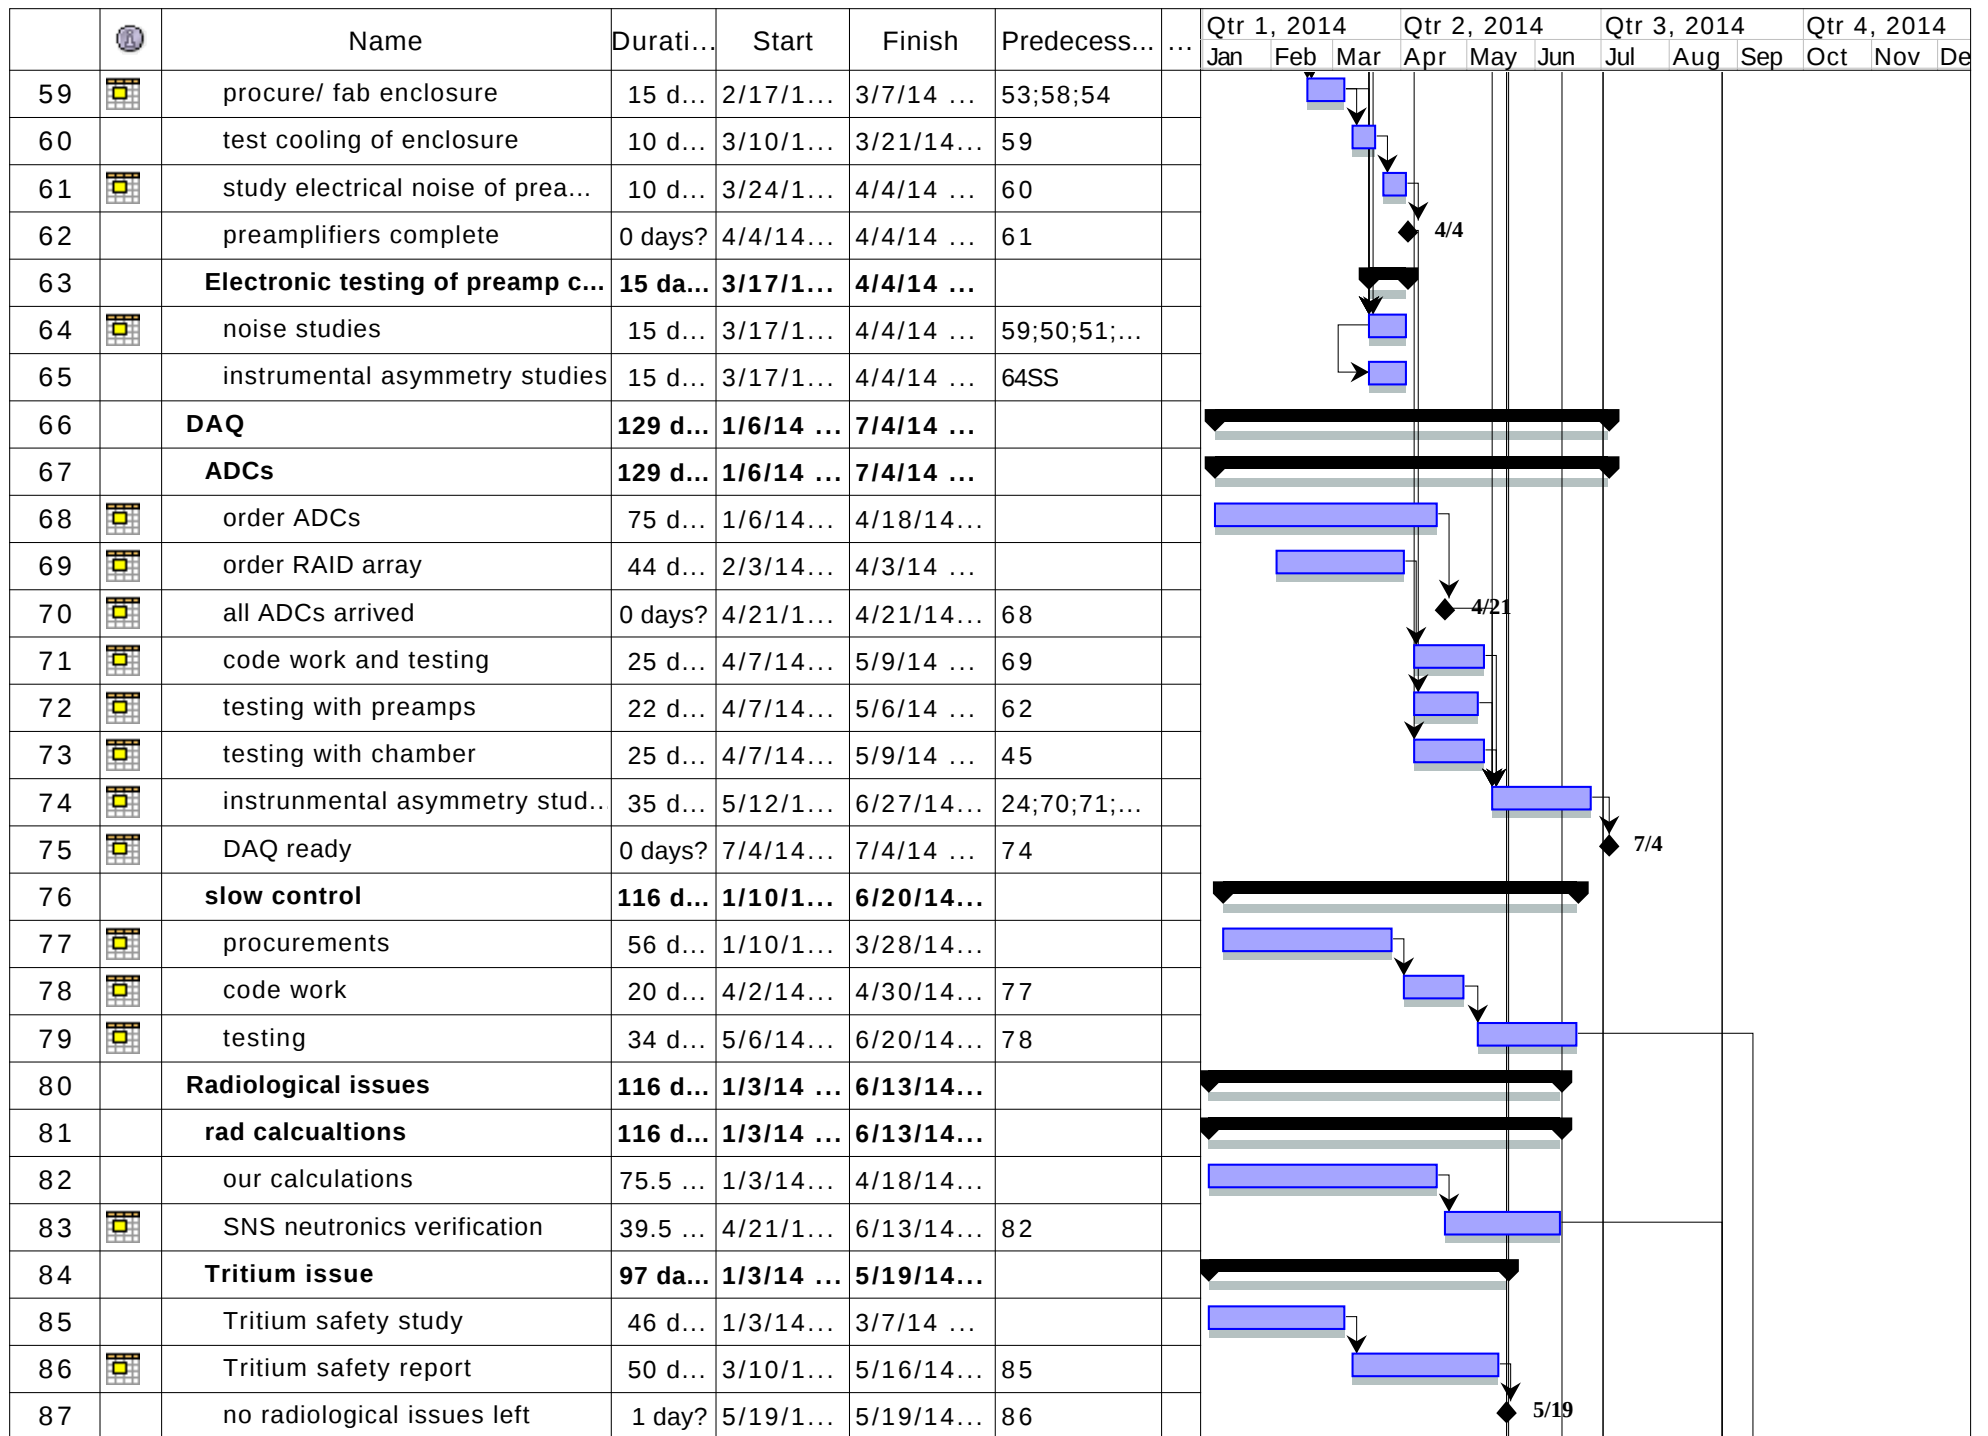

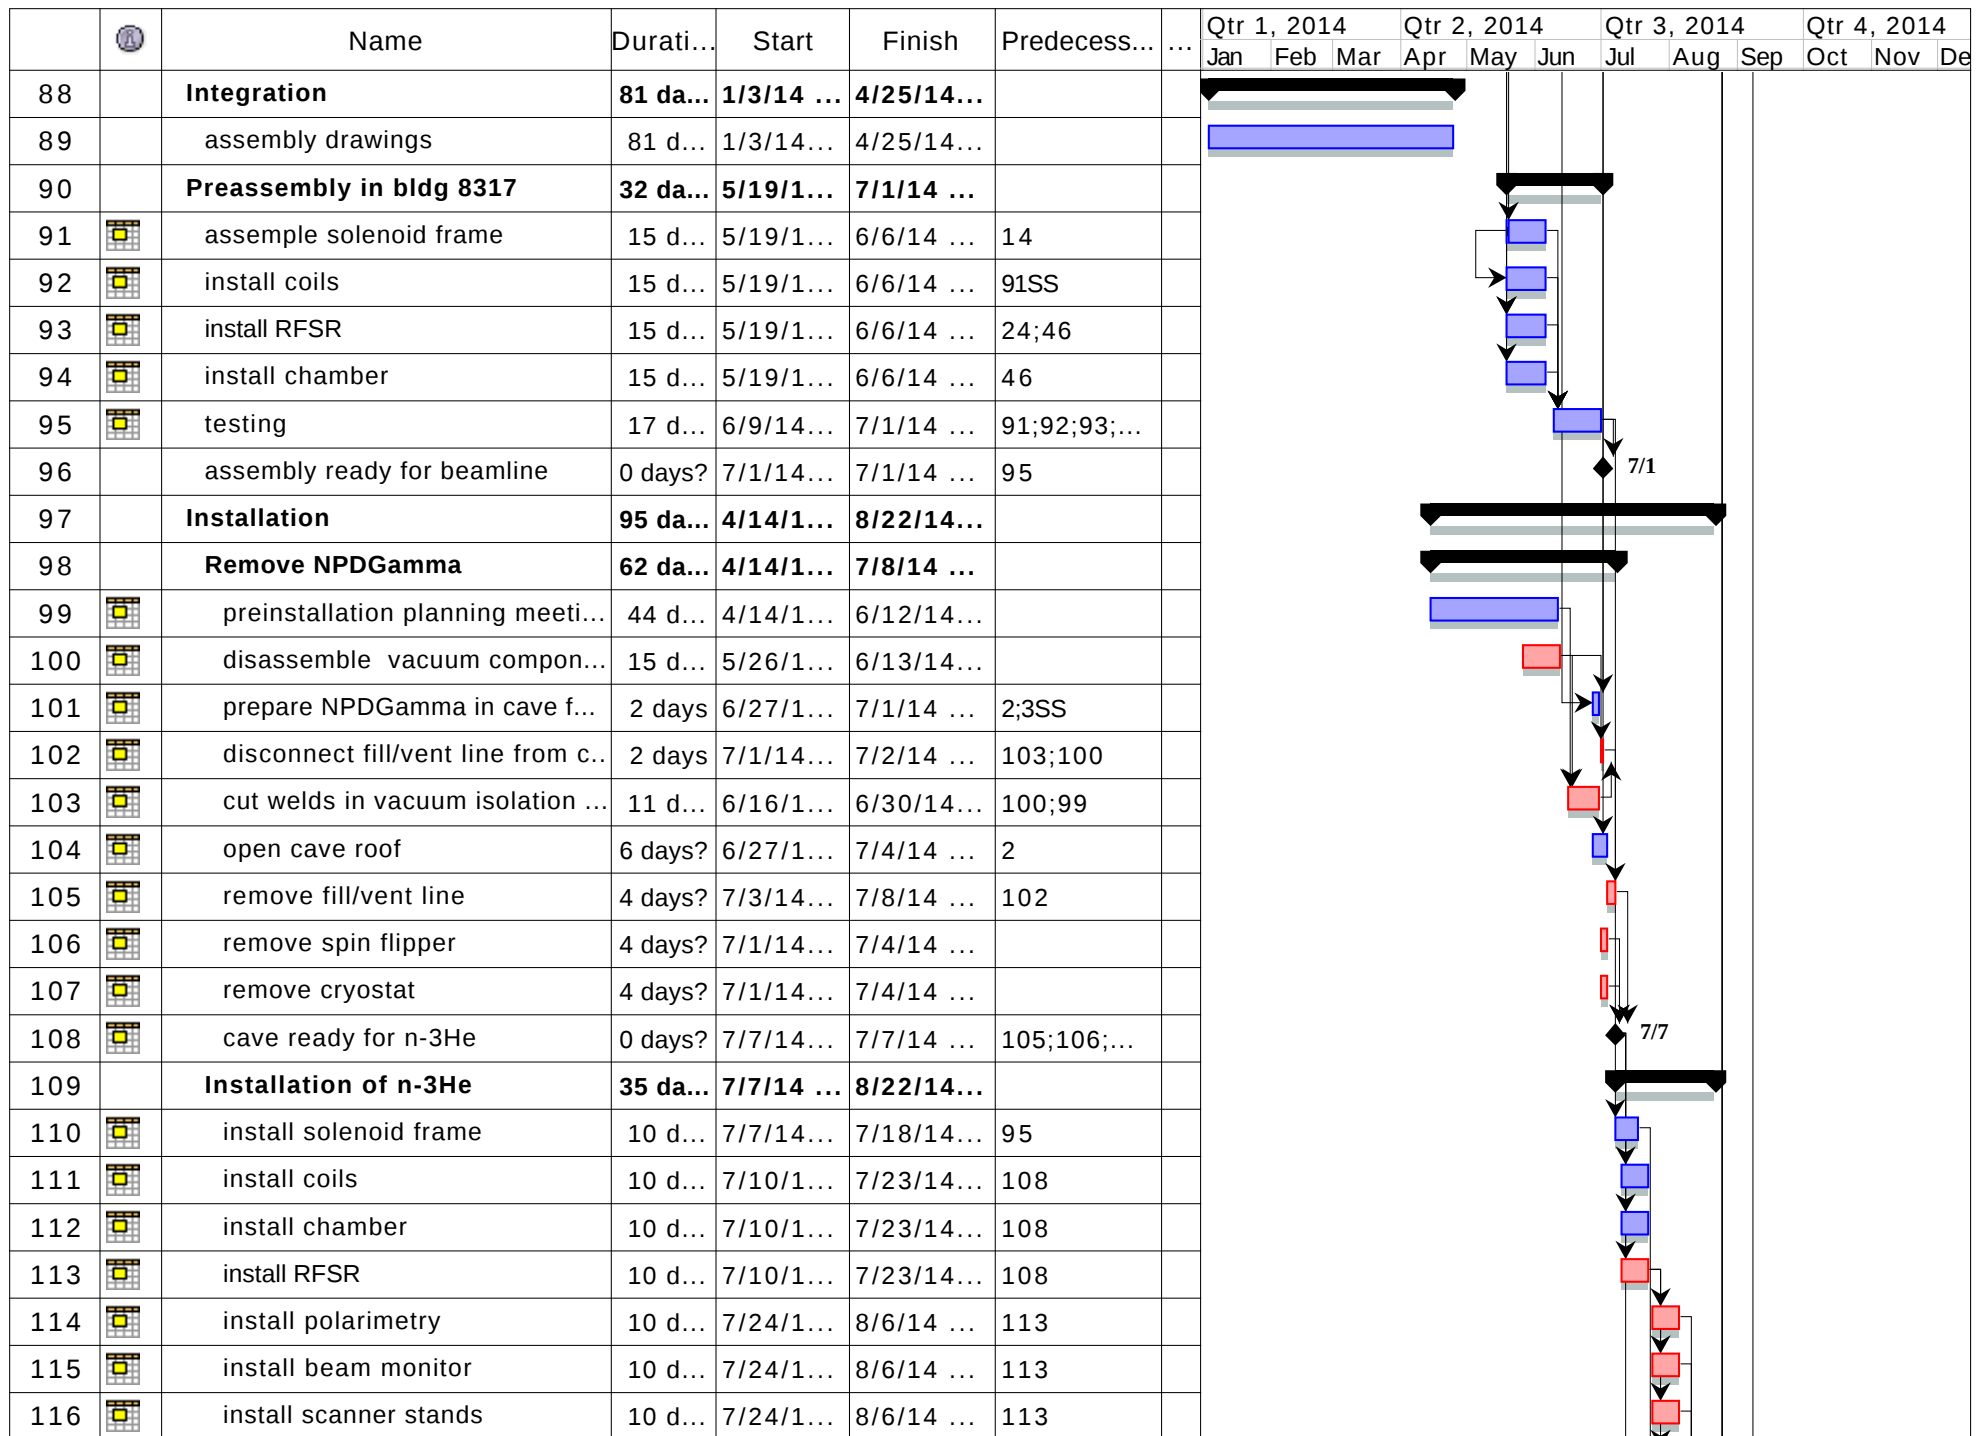

		Name	Durati...	Start	Finish	Predecess...	...	Qtr 1, 2014			Qtr 2, 2014			Qtr 3, 2014			Qtr 4, 2014		
								Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	De
117		install stand for alignment laser	10 d...	7/24/1...	8/6/14 ...	113													
118		install instrumentation	14 d...	7/7/14...	7/24/14...	108													
119		testing instrumentation	12 d...	8/7/14...	8/22/14...	118;117;...													
120		reinstall roof	20 d...	7/21/1...	8/15/14...	110													
121		n-3He installation complete	0 days?	8/22/1...	8/22/14...	119;120									8/22				
122		IRR process	90 da...	5/5/14 ...	9/8/14 ...														
123		preparations for IRR	78 d...	5/5/14...	8/20/14...														
124		main IRR	10 d...	8/25/1...	9/5/14 ...	4;7;83;12...													
125		beam authorized for commissio...	0 days?	9/8/14...	9/8/14 ...	124									9/8				
126		Construction project complete	0 day...	9/8/14 ...	9/8/14 ...										9/8				
127		construction complete	0 days?	9/8/14...	9/8/14 ...	79;124;125									9/8				
128		Commissioning	50 da...	9/8/14 ...	11/14/1...														
129		commissioning	50 d...	9/8/14...	11/14/1...	127													
130		commissioning complete	0 days?	11/14/...	11/14/1...	129									11/14				
131		Production	5 day...	11/17/...	11/21/1...														
132		IRR walk	5 days?	11/17/...	11/21/1...	130													
133		start production	0 days?	11/21/...	11/21/1...	132									11/21				

C

4

2

•
